


Midwest Breezes

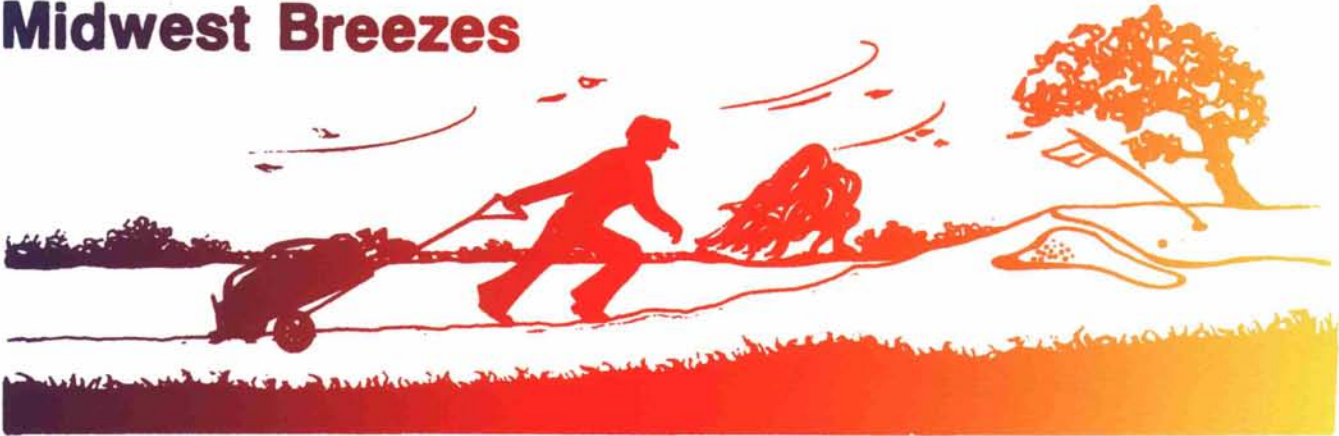

David Schlagetter, Indian Hill Club

This spring Dave went through all of his bunkers and added sand to provide a uniform depth of six inches in every section of every bunker. He also replaced the sand directly above the tile lines, and this has significantly improved his bunker drainage.

This project required 20 loads of sand and 750 man-hours for 69 bunkers.

-Brad Anderson, CGCS



A few of the crew at Indian Hill remove old sand from atop drain lines in a bunker. New sand is used to backfill the trench, increasing the porosity to the tile line, thus increasing overall drainage of the bunker.
